Roadmap - report date 29 Oct 2026 (red line) | Six weeks to 10 Dec | solid = done, outlined = to do, dotted = needs input

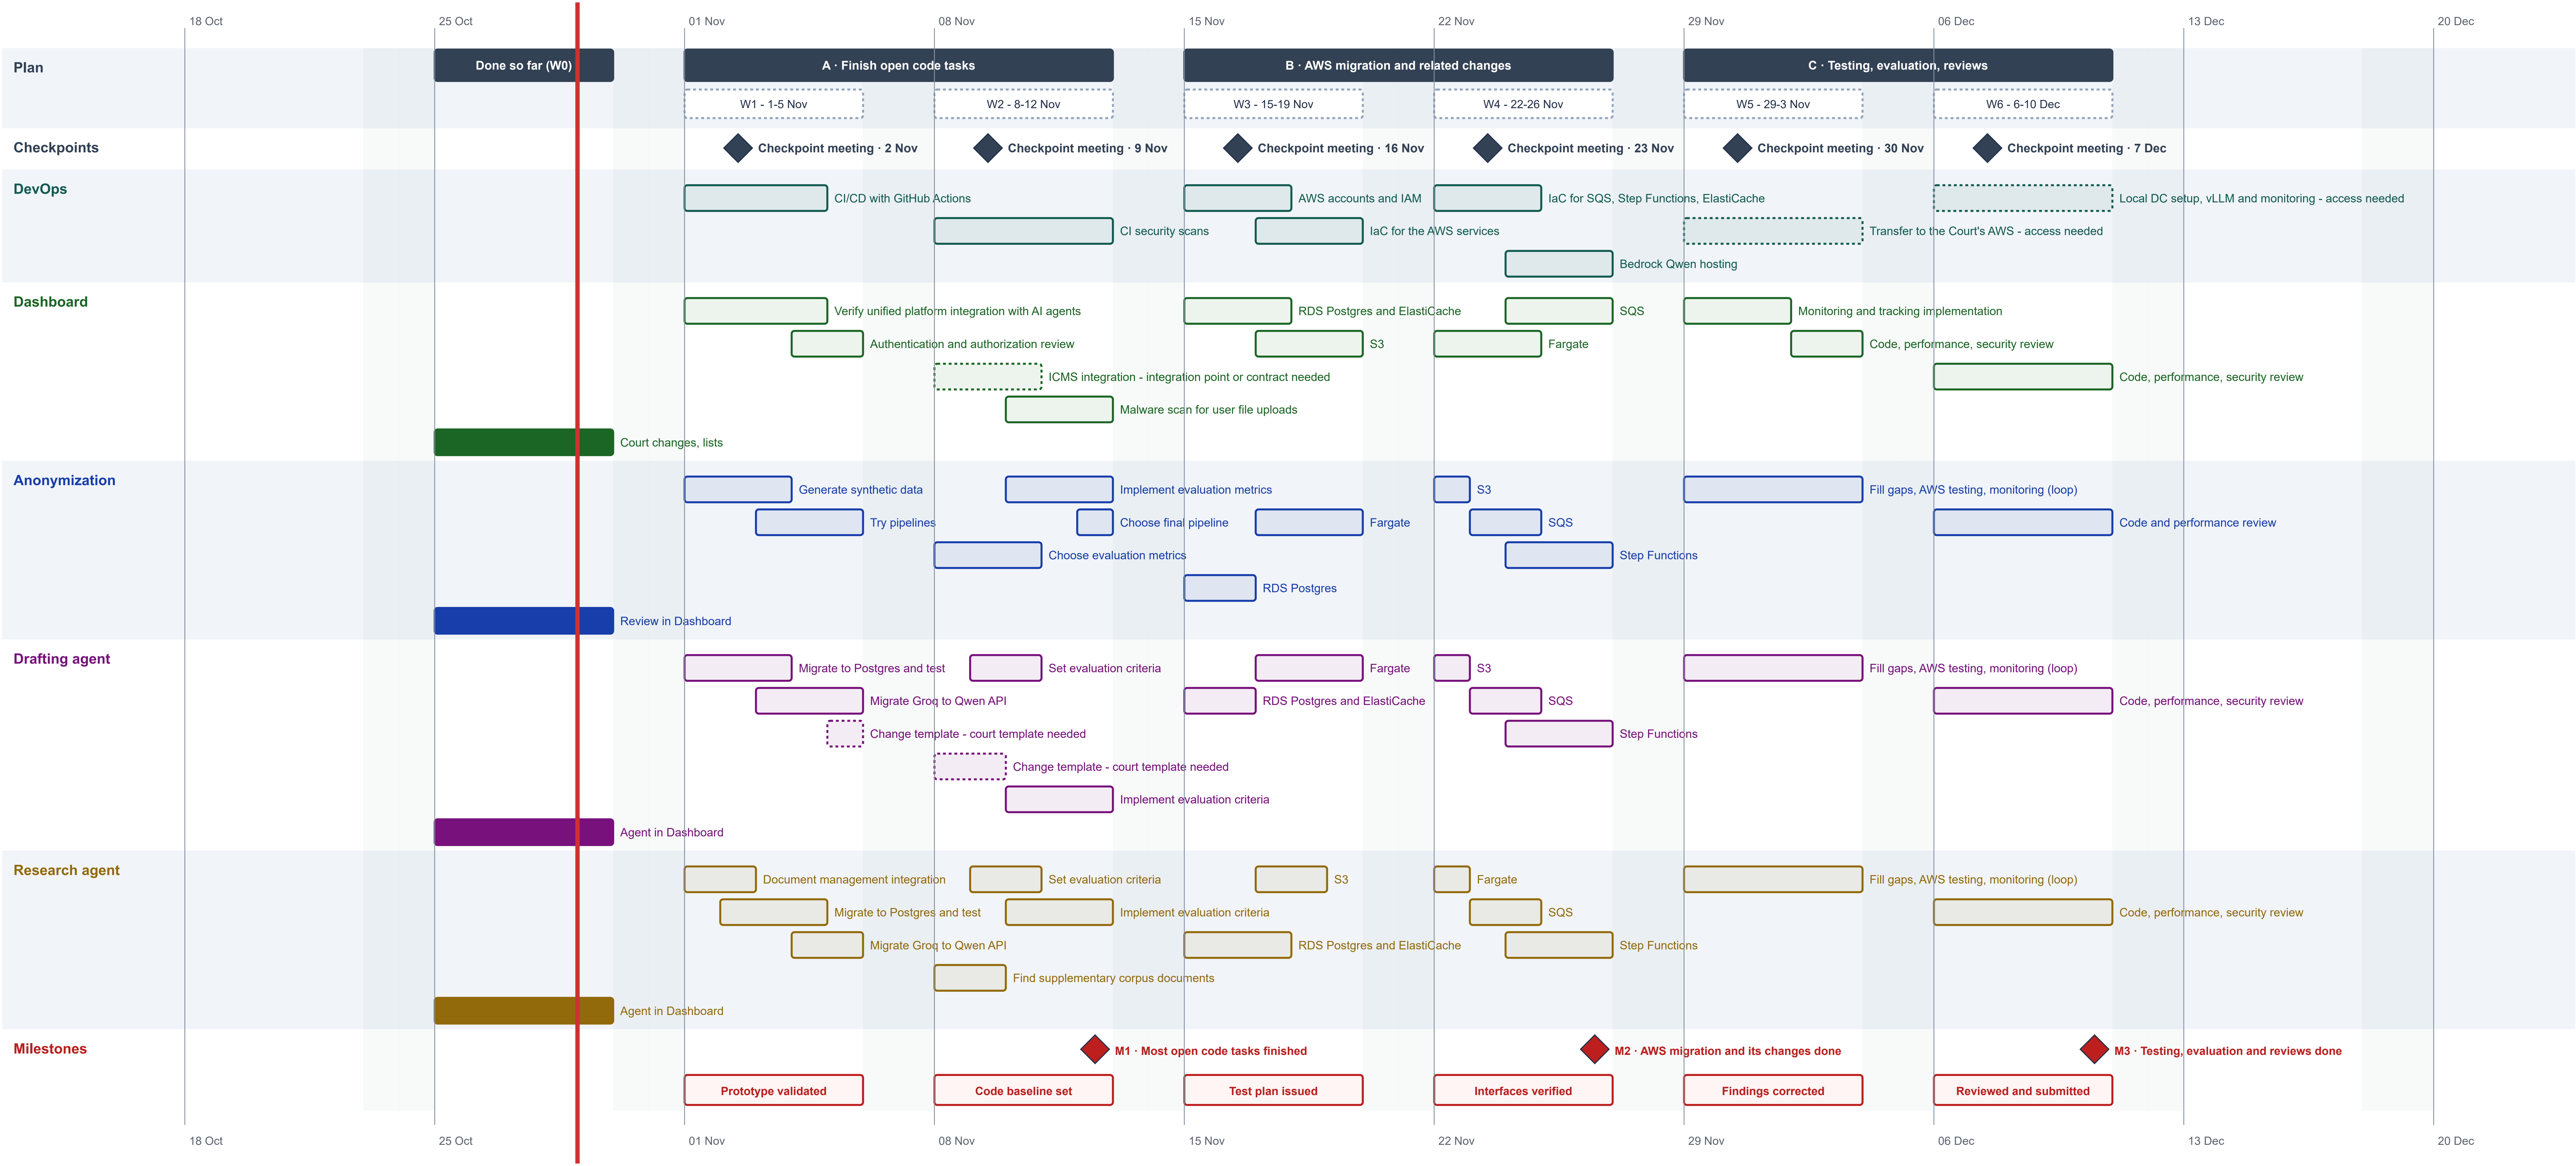
18 Oct
25 Oct
01 Nov
08 Nov
15 Nov
22 Nov
29 Nov
06 Dec
13 Dec
20 Dec
Plan
Done so far (W0)
A · Finish open code tasks
B · AWS migration and related changes
C · Testing, evaluation, reviews
W1 - 1-5 Nov
W2 - 8-12 Nov
W3 - 15-19 Nov
W4 - 22-26 Nov
W5 - 29-3 Nov
W6 - 6-10 Dec
Checkpoints
Checkpoint meeting · 2 Nov
Checkpoint meeting · 9 Nov
Checkpoint meeting · 16 Nov
Checkpoint meeting · 23 Nov
Checkpoint meeting · 30 Nov
Checkpoint meeting · 7 Dec
DevOps
CI/CD with GitHub Actions
AWS accounts and IAM
IaC for SQS, Step Functions, ElastiCache
Local DC setup, vLLM and monitoring - access needed
CI security scans
IaC for the AWS services
Transfer to the Court's AWS - access needed
Bedrock Qwen hosting
Dashboard
Verify unified platform integration with AI agents
RDS Postgres and ElastiCache
SQS
Monitoring and tracking implementation
Authentication and authorization review
S3
Fargate
Code, performance, security review
ICMS integration - integration point or contract needed
Code, performance, security review
Malware scan for user file uploads
Court changes, lists
Anonymization
Generate synthetic data
Implement evaluation metrics
S3
Fill gaps, AWS testing, monitoring (loop)
Try pipelines
Choose final pipeline
Fargate
SQS
Code and performance review
Choose evaluation metrics
Step Functions
RDS Postgres
Review in Dashboard
Drafting agent
Migrate to Postgres and test
Set evaluation criteria
Fargate
S3
Fill gaps, AWS testing, monitoring (loop)
Migrate Groq to Qwen API
RDS Postgres and ElastiCache
SQS
Code, performance, security review
Change template - court template needed
Step Functions
Change template - court template needed
Implement evaluation criteria
Agent in Dashboard
Research agent
Document management integration
Set evaluation criteria
S3
Fargate
Fill gaps, AWS testing, monitoring (loop)
Migrate to Postgres and test
Implement evaluation criteria
SQS
Code, performance, security review
Migrate Groq to Qwen API
RDS Postgres and ElastiCache
Step Functions
Find supplementary corpus documents
Agent in Dashboard
Milestones
M1 · Most open code tasks finished
M2 · AWS migration and its changes done
M3 · Testing, evaluation and reviews done
Prototype validated
Code baseline set
Test plan issued
Interfaces verified
Findings corrected
Reviewed and submitted
18 Oct
25 Oct
01 Nov
08 Nov
15 Nov
22 Nov
29 Nov
06 Dec
13 Dec
20 Dec
